



	BILL OF MATERIAL											
Qty Ea.	Qty Tot	Piece Mark	Description	Length	Weight Total	Remarks	Adv Mill #	Steel Grade				
	1	2B118	BEAM									
1	1		HSS10X10X3/8	20'-6"	921	SQ-2 STD PRIMER	hs6	A500-GR.B				
2	2	a1096	L5X3X3/8	10'-2 1/4"	198	STD PRIMER		A36				
1	1	hs8	HSS4X4X3/8	8'-9 5/16"	143	STD PRIMER		A500-GR.B				
1	1	hs22	HSS4X4X3/8	1'-0 11/16"	17	STD PRIMER		A500-GR.B				
7	7	p1086	PL3/8"X4"	0'-6"	18	STD PRIMER		A36				

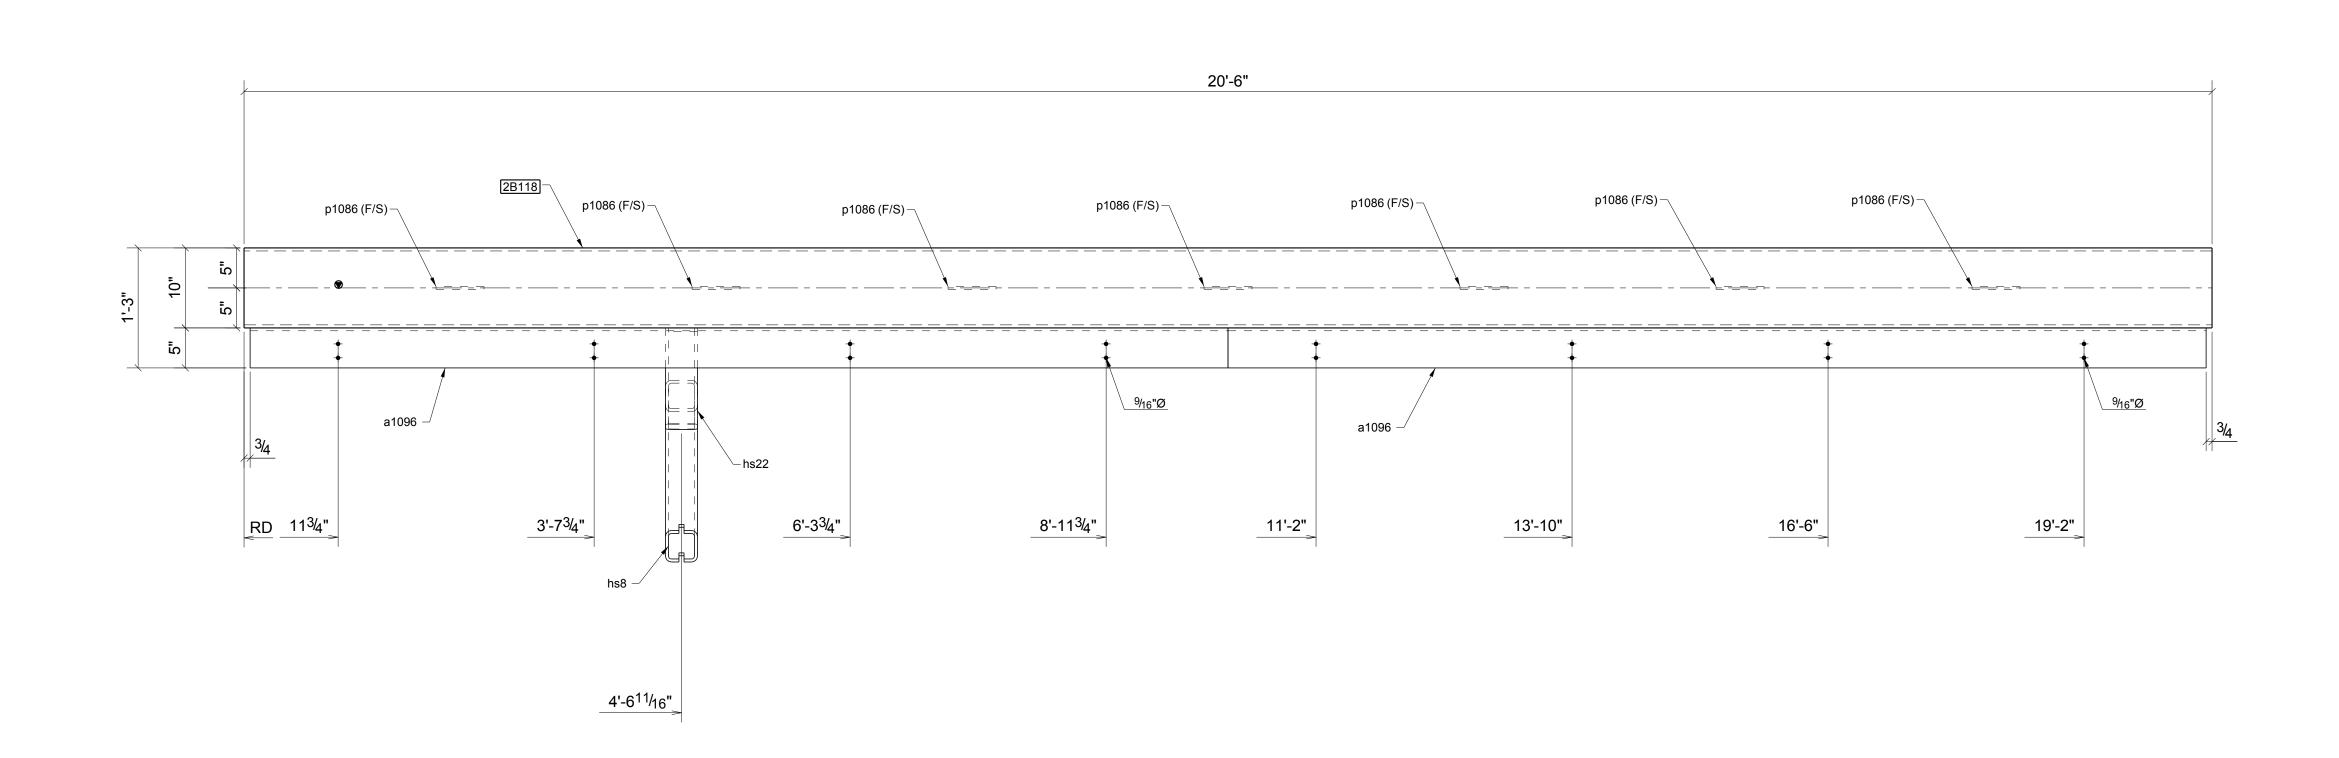

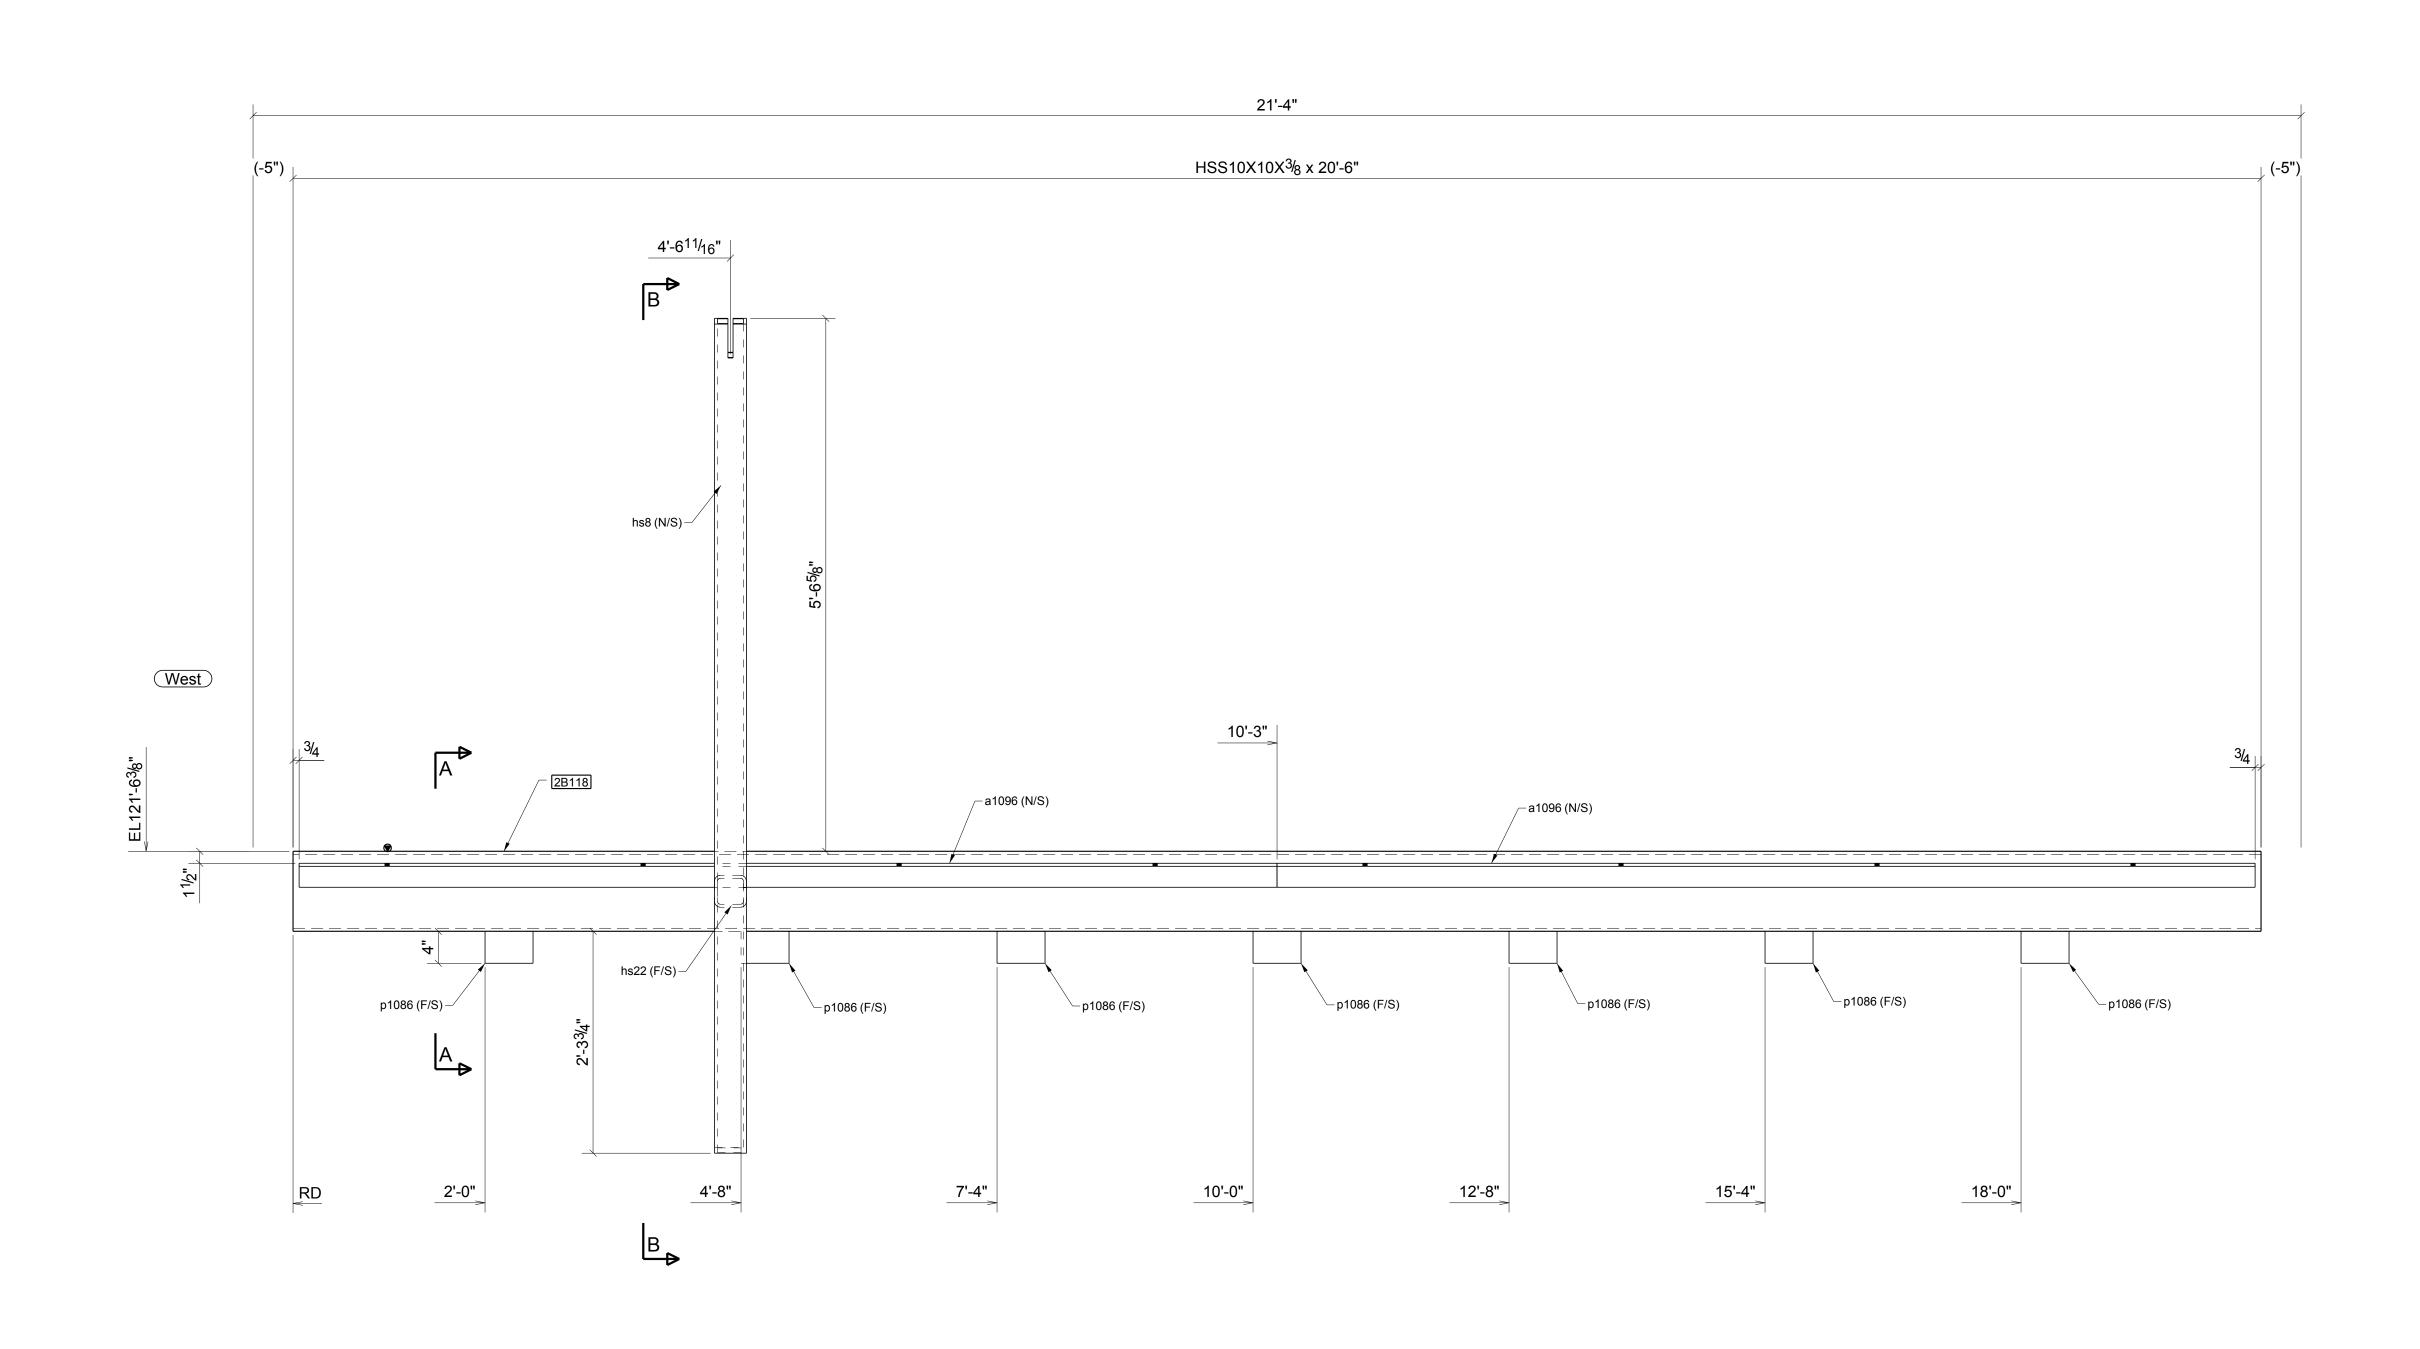

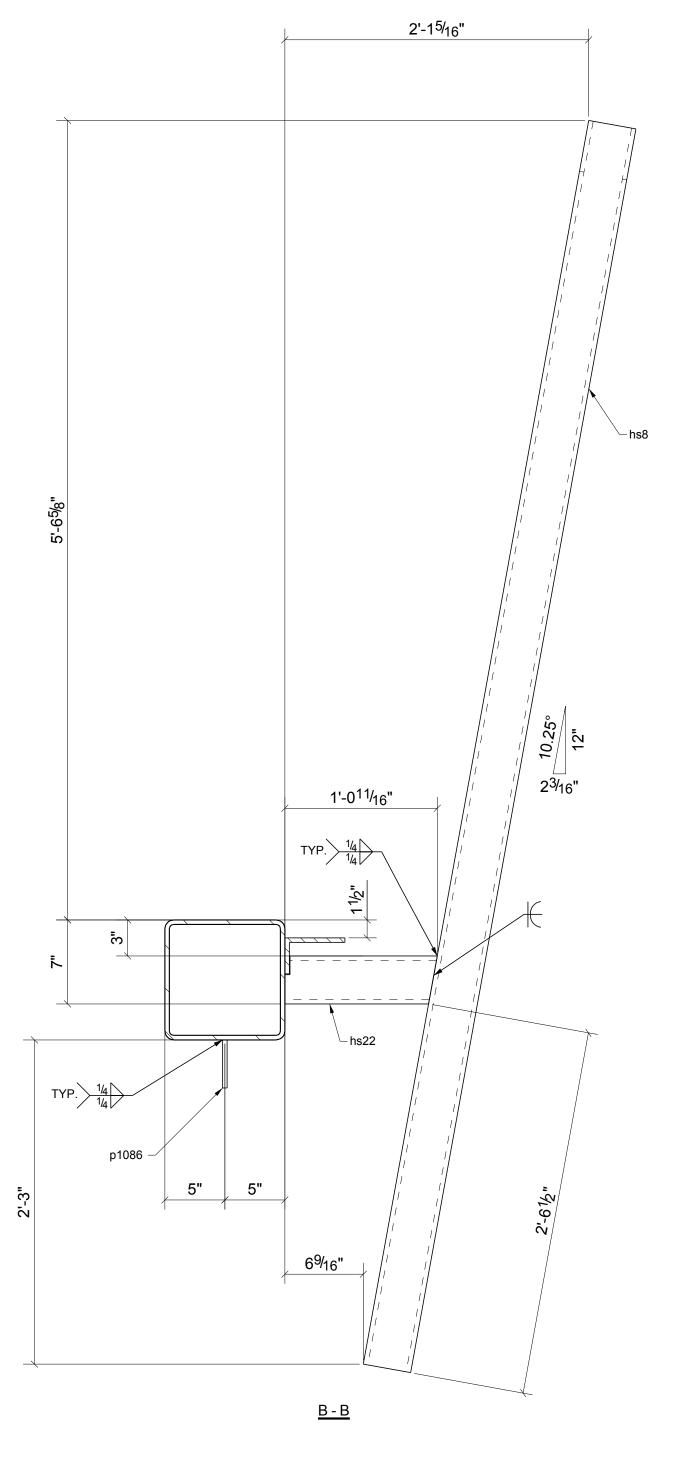

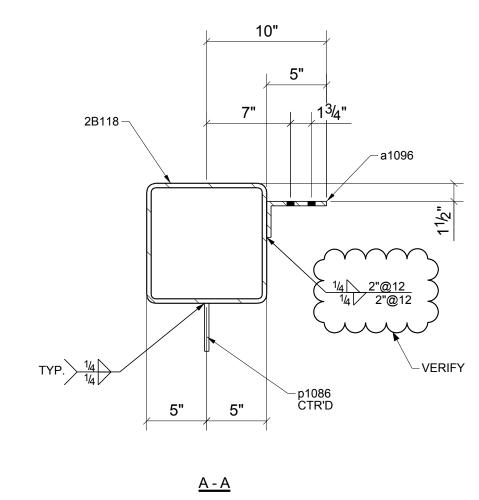

STD PRIMER ONE - BEAM - 2B118

REF DWGS: MP100

: MP100 TEKLA STRUCTURES



DWG.	ISSUE	REVISIONS		
DATE	PURPOSE	NO.	DATE	DESCRIPTION
03/14/2016	FOR APP	A		



Per AISC Steel Construction Manual 13th Edition 16.3.3 Commentary:

While it is the Fabricator's responsibility to report any discrepancies that are iscovered in the Contract Documents, it is not the Fabricator's responsibility to iscover discrepancies, including those that are associated with the coordination of the various design disciplines. The quality of the Contract Documents is the responsibility of the entities that produce those documents.
